

Sub-Project Management Plan for User Identity, Profile and Portfolio Management

Version 1.0 approved

Prepared by Ayesha Naveed

National University of Computer and Emerging Sciences

27th March,2026

Contents

1. Executive Summary	4
2. Project Scope	4
2.1 Project Summary and Justification.....	4
2.2 Project Objectives and Success Criteria	5
2.3 Product Scope Description	5
2.4 Product Characteristics and Requirements.....	5
2.5 User Acceptance Criteria	6
2.6 Project Deliverables	6
2.6.1 Product Deliverables	6
2.6.2 Project Management Deliverables.....	6
2.7 Project Boundaries.....	7
2.9 Assumptions.....	7
2.10 Schedule and Budget Information.....	7
2.11 Supporting References.....	8
2.12 Scope Management Note	8
3. Deliverables	8
3.1 Product Deliverables of Sub-Project	8
3.2 Process Deliverables of Sub-Project.....	9
4. Work Breakdown Structure (WBS).....	9
5. Stakeholder Analysis	10
5.1 Stakeholder Register	11
5.2 Stakeholder Analysis Table.....	11
5.3 Stakeholder Management Summary.....	12
6. Schedule Baseline	12
6.1 Gantt Chart	13
7. Milestone List	13
7.1 Milestone Table	13
7.2 Brief Explanation	14
8. Project Scope Management Plan	14
8.1 Scope Definition Process.....	14
8.2 Work Breakdown Structure (WBS) Development.....	14
8.3 WBS Maintenance and Approval.....	15

8.4 Scope Validation (Acceptance of Deliverables)	15
8.5 Scope Control (Change Management Process)	15
8.6 Summary.....	16
9. Project Staff List	16
9.1 Project Staff List Table	16
9.2 Task Allocation Strategy	16
9.3 Summary.....	17
10. Schedule Management Plan	17
10.1 Project Schedule Model Development.....	17
10.2 Level of Accuracy and Units of Measure	17
10.3 Control Thresholds	17
10.4 Rules of Performance Measurement	18
10.5 Reporting Formats.....	18
10.6 Schedule Control Process	18
10.7 Summary.....	19
11. Authorization Signatures	19

1. Executive Summary

The *User Identity, Profile & Portfolio Management Module* is a core sub-project of the National Freelance and Skill Verification Platform. This module is responsible for managing user identities and enabling freelancers and clients to create, maintain, and present their professional profiles within the system. It plays a critical role in establishing trust, credibility, and transparency across the platform.

The module supports multi-role user registration, including freelancers, clients, and administrators, along with secure authentication and profile management capabilities. Freelancers can build detailed professional profiles showcasing their skills, experience, work history, and portfolio. The module also enables users to upload project samples and maintain a structured record of completed work, allowing clients to effectively evaluate talent. Additionally, it incorporates a review and rating mechanism to reflect user credibility and performance.

This sub-project contributes directly to the overall objective of reducing fraud, improving skill visibility, and enhancing trust between stakeholders in the freelance ecosystem. By providing a standardized and professional representation of users, the module serves as a foundation for other system components such as job matching, skill verification, and payment services.

The development of this module will follow a structured project management approach, aligning with the overall system architecture and integration requirements defined at the project level. It is expected to be developed within the academic timeline through coordinated team efforts, ensuring scalability, usability, and seamless integration with other platform modules.

2. Project Scope

Sub-Project Title: User Identity, Profile & Portfolio Management Module

Date: 27-03-2026

Prepared By: Ayesha Naveed

2.1 Project Summary and Justification

This sub-project is part of the National Freelance and Skill Verification Platform, which aims to improve trust, transparency, and credibility in Pakistan's freelance ecosystem.

The User Identity, Profile & Portfolio Management Module is designed to provide a secure and structured mechanism for managing user identities and professional representation on the platform. It enables freelancers to showcase verified skills, experience, and past work, while allowing clients to evaluate potential candidates effectively.

This module is critical to reducing fraudulent profiles, improving visibility for skilled freelancers, and supporting informed decision-making for employers. It also serves as a foundational component for other modules such as job matching, skill verification, and payment services.

The sub-project will be developed within the academic semester timeline using available resources and will align with the overall system architecture defined by the integration group.

2.2 Project Objectives and Success Criteria

Objectives:

- Enable secure user registration and authentication for multiple roles
- Provide comprehensive profile and portfolio management features
- Improve trust and credibility through structured user data and ratings
- Ensure seamless integration with other system modules

Success Criteria:

- Module is completed within the defined academic schedule
- All core functionalities operate correctly and without critical defects
- Successful integration with dependent modules
- Positive user acceptance based on usability and functionality
- Minimal scope deviations and controlled changes

2.3 Product Scope Description

The module will provide functionality for user identity management and professional profile representation. It includes user registration, authentication, profile creation, portfolio management, work history tracking, and review systems.

Freelancers will be able to present their professional identity through structured profiles and portfolios, while clients can access and evaluate this information to make informed hiring decisions.

The system will ensure secure data handling, role-based access control, and efficient storage and retrieval of user-related data.

2.4 Product Characteristics and Requirements

1. **User Registration and Authentication**
The system shall support registration and login for freelancers, clients, and administrators with secure authentication mechanisms.
2. **Profile Management**
Users shall be able to create, edit, and manage detailed profiles including personal information, skills, and experience.
3. **Portfolio Management**
Freelancers shall be able to upload, update, and display portfolio items such as project samples, documents, and external links.
4. **Work History Tracking**
The system shall maintain records of completed projects and professional experience.

5. **Reviews and Ratings**

Clients shall be able to provide feedback and ratings for freelancers, which will be displayed on profiles.

6. **Role-Based Access Control**

The system shall enforce access restrictions based on user roles.

7. **Data Management**

The system shall securely store and efficiently retrieve all user-related data.

8. **Usability and Accessibility**

The module shall provide a user-friendly interface accessible via standard web browsers.

2.5 User Acceptance Criteria

The module will be accepted when:

- Users can successfully register and log in based on their roles
- Profiles can be created, updated, and viewed without errors
- Portfolio items can be uploaded and displayed correctly
- Work history is accurately recorded and retrievable
- Ratings and reviews are properly reflected on user profiles
- Security and access control requirements are satisfied

2.6 Project Deliverables

2.6.1 Product Deliverables

- User registration and authentication system
- Profile management system
- Portfolio management functionality
- Work history tracking feature
- Review and rating system
- Database schema for user-related data
- APIs for integration with other modules
- User interface for profile and portfolio display
- Testing and validation reports

2.6.2 Project Management Deliverables

- Scope statement
- Work Breakdown Structure (WBS)
- Schedule baseline and Gantt chart
- Milestone list
- Progress reports
- Final project report

2.7 Project Boundaries

In Scope:

- User identity management (registration and login)
- Profile creation, editing, and viewing
- Portfolio and project sample management
- Work history tracking
- Reviews and ratings

Out of Scope:

- Skill assessment and certification
- Job posting and matching
- Payment and escrow services
- Advanced analytics and reporting

2.8 Constraints

- Limited development time (one academic semester)
- Limited team size and academic resources
- Dependency on other modules for integration
- Use of open-source tools and technologies
- No real-world financial or legal system implementation

2.9 Assumptions

- Users will provide accurate and complete information
- Other modules will be developed and available for integration
- Standard technologies will be sufficient for implementation
- Users will have access to internet-enabled devices
- Initial system load will be manageable

2.10 Schedule and Budget Information

Schedule:

The module will be developed within the overall project timeline of approximately 3 months, including planning, design, development, testing, and integration phases.

Budget:

As an academic project, no direct financial budget is allocated. Development will utilize open-source tools and institutional resources. Effort is distributed among team members as per assigned tasks.

2.11 Supporting References

- Business Case (Assignment 1)
- Module decomposition document
- Project Charter
- Software Requirements Specification (SRS)
- Software Design Specification (SDS)

2.12 Scope Management Note

This scope statement will be progressively elaborated and refined throughout the project lifecycle. Any changes to scope will be formally reviewed and controlled to prevent scope creep and ensure alignment with overall project objectives.

3. Deliverables

3.1 Product Deliverables of Sub-Project

The following product deliverables represent the functional outputs of the *User Identity, Profile & Portfolio Management Module*:

1. **User Registration and Authentication System**
A fully functional system supporting multi-role registration (freelancer, client, admin) with secure login and authentication mechanisms.
2. **User Profile Management System**
Interfaces and backend services enabling users to create, update, and manage detailed professional profiles including personal information, skills, and experience.
3. **Portfolio Management System**
Functionality allowing freelancers to upload, edit, delete, and display portfolio items such as project samples, documents, and external links.
4. **Work History Tracking Feature**
A structured system for maintaining records of completed projects and professional experience.
5. **Review and Rating System**
Mechanism for clients to provide feedback and ratings, which are stored and displayed on freelancer profiles.
6. **Database Design and Implementation**
Database schema and storage mechanisms for managing user identities, profiles, portfolios, and reviews.
7. **APIs for Integration**
Well-defined API endpoints to enable integration with other modules such as job matching, skill verification, and payment services.
8. **User Interface Components**
Frontend interfaces for registration, profile management, and portfolio display, ensuring usability and accessibility.
9. **Testing and Validation Artifacts**
Test cases, test results, and bug reports ensuring that all module functionalities meet specified requirements.

3.2 Process Deliverables of Sub-Project

The following deliverables are related to project management, planning, and execution of the sub-project:

1. **Sub-Project Management Plan (SPMP)**
A comprehensive plan including scope, schedule, WBS, stakeholders, and management strategies for the module.
2. **Work Breakdown Structure (WBS)**
A detailed decomposition of all tasks required to complete the module.
3. **Schedule Baseline and Gantt Chart**
A planned timeline for task execution, dependencies, and milestones.
4. **Milestone List**
Identification of key milestones such as completion of design, development, testing, and integration phases.
5. **Progress Reports**
Periodic updates documenting development progress, issues, and risks.
6. **Requirements Management Plan (SP-RMP)**
Documentation outlining how requirements will be collected, managed, and tracked.
7. **Software Requirements Specification (SP-SRS)**
Detailed documentation of functional and non-functional requirements of the module.
8. **Software Design Specification (SP-SDS)**
Technical design document describing system architecture, components, and interactions.
9. **Testing Plan**
A plan outlining testing strategies, responsibilities, and defect tracking mechanisms.
10. **Final Project Report and Demonstration**
Documentation and presentation summarizing the completed module, its features, and performance.

4. Work Breakdown Structure (WBS)

1.0 User Identity, Profile & Portfolio Management Module

1.1 Project Management

- 1.1.1 Planning
- 1.1.2 Meetings & Coordination
- 1.1.3 Progress Tracking & Reporting

1.2 Requirements Analysis

- 1.2.1 Requirement Gathering
- 1.2.2 Requirement Analysis
- 1.2.3 Requirement Documentation (SRS)

1.3 System Design

- 1.3.1 System Architecture Design
- 1.3.2 Database Design (User, Profile, Portfolio)
- 1.3.3 API Design
- 1.3.4 UI/UX Design

1.4 Development – User Identity Management

- 1.4.1 User Registration Implementation
- 1.4.2 Authentication (Login/Logout)
- 1.4.3 Role-Based Access Control

1.5 Development – Profile Management

- 1.5.1 Profile Creation Feature
- 1.5.2 Profile Editing Feature
- 1.5.3 Profile Viewing Feature

1.6 Development – Portfolio Management

- 1.6.1 Portfolio Upload Feature
- 1.6.2 Portfolio Edit/Delete Feature
- 1.6.3 Portfolio Display Interface

1.7 Development – Work History & Reviews

- 1.7.1 Work History Tracking
- 1.7.2 Review & Rating System

1.8 Integration & API Development

- 1.8.1 API Implementation
- 1.8.2 Integration with Other Modules

1.9 Testing

- 1.9.1 Unit Testing
- 1.9.2 Integration Testing
- 1.9.3 System Testing
- 1.9.4 Bug Fixing

1.10 Documentation

- 1.10.1 SP-SRS Preparation
- 1.10.2 SP-SDS Preparation
- 1.10.3 Technical Documentation

1.11 Deployment & Demonstration

- 1.11.1 Deployment Setup
- 1.11.2 Final Demonstration
- 1.11.3 Final Report Submission

5. Stakeholder Analysis

Stakeholder analysis is conducted to identify all individuals and groups involved in or affected by the sub-project, assess their level of interest and influence, and define strategies to manage their expectations. Effective stakeholder management ensures smooth coordination, minimizes risks, and supports successful module delivery and integration.

5.1 Stakeholder Register

Name / Stakeholder	Position / Role	Internal / External	Project Role	Contact Information
Integration Group	System Integrators	Internal	Integration and coordination of all modules	-
Project Instructor	Supervisor / Evaluator	External	Provides guidance and evaluates deliverables	-
Module Team Members	Developers & Designers	Internal	Development of Module 1	-
Other Module Teams	Development Teams	Internal	Provide/consume APIs and data	-
Freelancers (End Users)	Platform Users	External	Create profiles and portfolios	N/A
Clients / Employers	Platform Users	External	Evaluate freelancers	N/A
Admin Users	System Administrators	Internal/External	Manage and moderate platform data	N/A

5.2 Stakeholder Analysis Table

Name / Stakeholder	Power / Interest	Current Engagement	Potential Management Strategies
Integration Group	High / High	Leading	The integration group coordinates all modules and ensures system compatibility. Maintain close communication, provide regular updates, and align APIs and deliverables with integration requirements.
Project Instructor	High / High	Leading	The instructor defines expectations and evaluates outcomes. Follow guidelines strictly, incorporate feedback promptly, and ensure all deliverables meet required standards.
Module Team Members	Medium / High	Supportive	Team members are actively involved in development. Assign clear responsibilities, conduct regular meetings, and monitor progress to maintain efficiency and accountability.
Other Module Teams	High / Medium	Neutral	These teams depend on this module for integration. Maintain coordination through clear API documentation and early resolution of dependencies to avoid delays.
Freelancers (End Users)	Medium / High	Neutral	Freelancers rely on this module to showcase their profiles. Ensure user-friendly design, reliable functionality, and complete features to encourage adoption and satisfaction.
Clients / Employers	Medium / High	Neutral	Clients use the module to evaluate freelancers. Ensure accurate profile representation, portfolio visibility, and trustworthy rating systems.
Admin Users	Medium / Medium	Supportive	Admins manage user data and platform control. Provide effective tools for moderation and ensure proper role-based access control.

5.3 Stakeholder Management Summary

Stakeholders with **high power and high interest**, such as the Integration Group and Project Instructor, will be closely managed through continuous communication and alignment.

Stakeholders with **high power but moderate interest**, such as other module teams, will be kept satisfied by ensuring smooth coordination and dependency management.


End users, including freelancers and clients, have **high interest but moderate power**, and their needs will be addressed by focusing on usability, reliability, and functionality. Internal stakeholders such as team members and administrators will be regularly engaged and informed to ensure effective execution and system management.

6. Schedule Baseline

The schedule baseline defines the planned start and finish dates for all major activities of the sub-project. The project follows the overall timeline agreed in the kickoff meeting, starting on **12 March 2026** and ending on **8 May 2026**.

WBS Code	Activity	Start Date	End Date	Duration
1.1	Project Management	12 Mar	8 May	Ongoing
1.2	Requirements Analysis	16 Mar	20 Mar	5 days
1.3	System Design	28 Mar	2 Apr	6 days
1.4	Development – User Identity Management	3 Apr	10 Apr	8 days
1.5	Development – Profile Management	11 Apr	18 Apr	8 days
1.6	Development – Portfolio Management	19 Apr	25 Apr	7 days
1.7	Development – Work History & Reviews	19 Apr	25 Apr	7 days
1.8	Integration & API Development	26 Apr	30 Apr	5 days
1.9	Testing	1 May	5 May	5 days
1.10	Documentation	21 Mar	7 May	Ongoing
1.11	Deployment & Demonstration	6 May	8 May	3 days

6.1 Gantt Chart

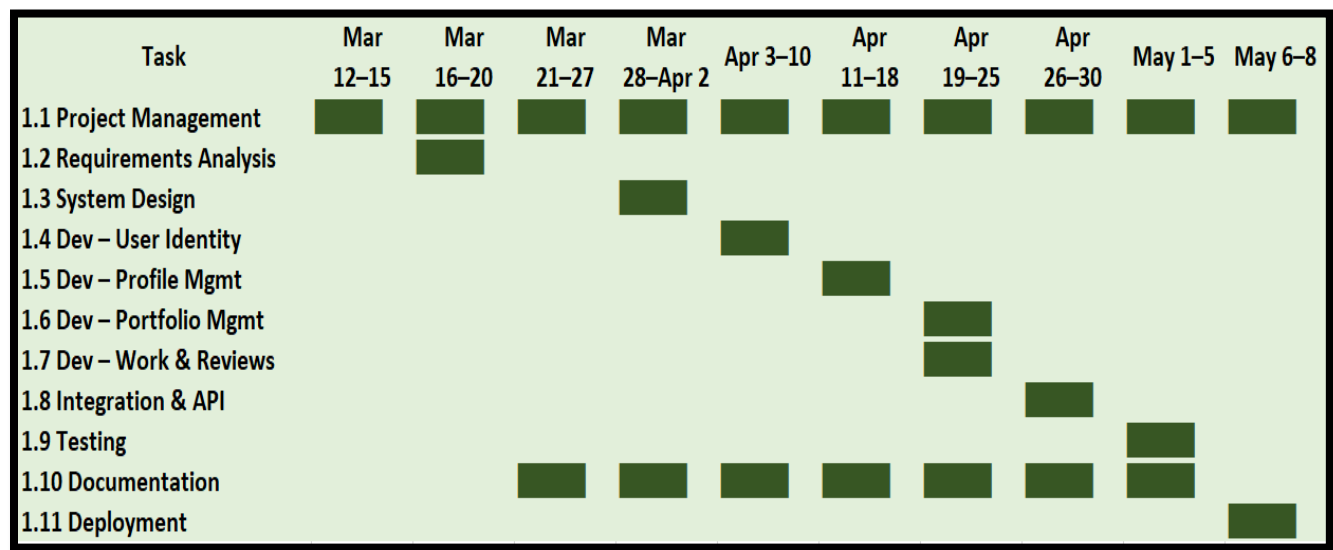

7. Milestone List

The following milestones represent key checkpoints in the sub-project lifecycle. These milestones help track progress, ensure alignment with the overall project schedule, and facilitate timely completion of major deliverables.

7.1 Milestone Table

Milestone ID	Milestone Name	Description	Planned Date
M1	Project Kickoff	Initial project discussion, team formation, and scope understanding	12 Mar 2026
M2	Requirements Finalized	Completion of requirement gathering and analysis for the module	20 Mar 2026
M3	SPMP & SRS Completion	Completion of major documentation (SPMP and SRS drafts)	27 Mar 2026
M4	System Design Completion	Finalization of architecture, database, API, and UI/UX design	2 Apr 2026
M5	User Identity Module Complete	Implementation of registration, authentication, and role management	10 Apr 2026
M6	Profile Management Complete	Profile creation, editing, and viewing features completed	18 Apr 2026
M7	Portfolio & Reviews Complete	Portfolio features, work history, and review system completed	25 Apr 2026
M8	Integration Ready	APIs implemented and module ready for integration with other modules	30 Apr 2026

M9	Testing Complete	Unit, integration, and system testing completed with bug fixes	5 May 2026
M10	Final Deployment & Submission	Module deployment, final demo, and report submission	8 May 2026

7.2 Brief Explanation

These milestones are aligned with the project schedule and WBS, ensuring that each major phase—planning, design, development, integration, testing, and deployment—is completed within the defined timeline. Achieving these milestones will ensure timely delivery and successful integration of the module within the overall system.

8. Project Scope Management Plan

The Scope Management Plan defines how the scope of the sub-project will be defined, developed, monitored, and controlled throughout the project lifecycle. It ensures that all required work—and only the required work—is included in the project.

8.1 Scope Definition Process

The project scope will be defined based on:

- The approved **Business Case (Assignment 01)**
- Functional requirements of **Module 1**
- Inputs from the **Integration Group and other modules**

A detailed **Scope Statement** will be prepared using standard templates provided in the course. The scope will clearly define:

- Features such as user registration, profile management, portfolio, and reviews
- Deliverables and acceptance criteria
- Project boundaries (in-scope and out-of-scope items)

The level of detail will be sufficient to guide development and avoid ambiguity.

8.2 Work Breakdown Structure (WBS) Development

The WBS will be created by decomposing the module into smaller, manageable components based on:

- Major functionalities (identity, profile, portfolio, reviews)
- Development phases (design, implementation, testing, integration)

Standard WBS guidelines will be followed:

- Use of hierarchical structure (Level 1 → Level 3)
- Each work package will be clearly defined and measurable

The WBS will serve as the foundation for scheduling, resource allocation, and progress tracking.

8.3 WBS Maintenance and Approval

The WBS will be reviewed and approved by:

- Module team members
- Integration group (for alignment)
- Instructor (if required)

Any updates to the WBS will be:

- Documented properly
- Communicated to all stakeholders
- Reflected in related documents (schedule, deliverables, etc.)

Version control will be maintained to track changes.

8.4 Scope Validation (Acceptance of Deliverables)

Formal acceptance of deliverables will be obtained through:

- Review of completed features against defined requirements
- Demonstrations of module functionality
- Feedback from the instructor and integration group

A deliverable will be considered accepted when:

- It meets functional requirements
- It passes testing successfully
- It aligns with integration requirements

8.5 Scope Control (Change Management Process)

All changes to the project scope will be managed through a formal change control process:

1. **Change Request Submission**
Any stakeholder can propose a change with proper justification.
2. **Impact Analysis**
The team will evaluate the impact on:
 - Schedule
 - Resources
 - Integration with other modules

3. Approval Process

Changes will be reviewed and approved by:

- Team lead
- Integration group (if cross-module impact exists)
- Instructor (if required)

4. Implementation and Documentation

Approved changes will be implemented and reflected in:

- Scope statement
- WBS
- Schedule baseline

Unauthorized scope changes will not be allowed to prevent scope creep.

8.6 Summary

This scope management plan ensures that the sub-project remains focused, controlled, and aligned with overall project objectives. By clearly defining scope processes and managing changes effectively, the team will minimize risks and ensure successful delivery of Module 1.

9. Project Staff List

The following table presents the team members along with their assigned roles and responsibilities. Task assignments are directly derived from the **Work Breakdown Structure (WBS)** to ensure clarity, accountability, and proper workload distribution.

9.1 Project Staff List Table

Name	Role	Assigned Responsibilities
Ayesha Naveed	Team Lead / Project Manager	Leads Project Management (1.1.1–1.1.3) including planning, coordination, and reporting; oversees Requirements Analysis (1.2) and System Design (1.3) ; manages communication with integration group (1.8.2); contributes to development tasks (1.4–1.7)
Minahil Fatima	Software Developer	Responsible for User Identity & Profile Development (1.4, 1.5) including registration (1.4.1), authentication (1.4.2), role management (1.4.3), profile creation/editing/viewing (1.5.1–1.5.3); contributes to Testing (1.9.1) and Documentation (1.10.1)
Usman Gohar	Software Developer	Responsible for Portfolio & Reviews Development (1.6, 1.7) including portfolio features (1.6.1–1.6.3), work history (1.7.1), and review system (1.7.2); leads API Development & Integration (1.8.1–1.8.2) ; contributes to Integration Testing (1.9.2)
Abdulah Tariq	Software Developer	Responsible for UI/UX Design (1.3.4) and frontend implementation for all modules; leads Testing (1.9.3–1.9.4) including system testing and bug fixing; contributes to Documentation (1.10.2–1.10.3) and Deployment (1.11.1–1.11.3)

9.2 Task Allocation Strategy

- Task assignments are directly mapped to **WBS work packages (1.x.x)** to ensure traceability.

- Development work (1.4–1.7) is distributed across team members but supported collaboratively.
- The team lead is responsible for **project management (1.1)** and **integration coordination (1.8.2)**.
- Testing (1.9) and documentation (1.10) are shared but led by specific members for accountability.
- Integration and deployment tasks ensure alignment with other modules in the system.

9.3 Summary

This staffing plan ensures that all WBS work packages are clearly assigned to team members, providing accountability while maintaining a collaborative development approach. It supports efficient execution, proper tracking, and successful delivery of the sub-project.

10. Schedule Management Plan

The Schedule Management Plan defines how the project schedule will be developed, monitored, and controlled throughout the lifecycle of the sub-project. It ensures timely completion of activities and alignment with the overall project deadline.

10.1 Project Schedule Model Development

The project schedule is developed based on the **Work Breakdown Structure (WBS)**, where each major activity is identified and sequenced logically.

A schedule model is created by:

- Defining project activities from the WBS
- Estimating the duration of each activity
- Identifying dependencies between tasks (e.g., design before development)
- Assigning start and end dates

The schedule baseline and Gantt chart are used as the primary tools for representing the project timeline.

10.2 Level of Accuracy and Units of Measure

- Time estimates are measured in **days**.
- The level of accuracy for activity duration is estimated within a reasonable range considering the academic project environment.
- Minor variations in duration are acceptable as long as the overall project deadline (**8 May 2026**) is met.

10.3 Control Thresholds

Schedule performance will be monitored using variance thresholds:

- A variance of **±10%** from the planned schedule is acceptable.

- Any delay beyond this threshold will require corrective action.

Corrective actions may include:

- Reallocation of tasks
- Increasing parallel work
- Adjusting non-critical activities

10.4 Rules of Performance Measurement

Project progress will be tracked using:

- **Percentage completion of tasks**
- Completion of defined milestones
- Comparison of planned vs actual progress

Each task will be considered complete only when:

- All required functionalities are implemented
- Testing is completed successfully

10.5 Reporting Formats

Schedule progress will be communicated through:

- **Weekly progress updates** within the team
- Coordination updates with the **integration group**
- Informal reports and discussions during meetings

The Gantt chart and milestone list will be used to visually track progress.

10.6 Schedule Control Process

Schedule control will be managed through the following process:

1. **Monitoring Progress**
Regular comparison of actual progress against the schedule baseline
2. **Identifying Variances**
Detecting delays or deviations from planned timelines
3. **Analyzing Impact**
Evaluating the effect of delays on dependent tasks and integration
4. **Taking Corrective Actions**
Adjusting task assignments, timelines, or priorities
5. **Updating Schedule Documents**
Reflecting approved changes in the schedule baseline and Gantt chart

10.7 Summary

This schedule management plan ensures that the project timeline is realistic, continuously monitored, and effectively controlled. By following structured scheduling practices, the team aims to complete all activities within the defined timeframe and ensure successful delivery of the module.

11. Authorization Signatures

The undersigned acknowledge that they have reviewed and approved this Sub-Project Management Plan (SPMP) for the *User Identity, Profile & Portfolio Management Module*.

Name	Role	Signature	Date
Ayesha Naveed	Team Lead	Ayesha Naveed	27 / 03 / 2026
